


Jersey Village 3 Day Plan 10-19-2023

### **Underground Work**

- Centerpoint Energy has finally released construction after trouble locating gas main.
- Excavation Began 10-17, will continue through end of week.
- Boring, and Excavation along Senate Ave between Singapore Ln and Dillard Dr.
- Boring and Excavation in Rear Easement of 15809 – 15905 Seattle St

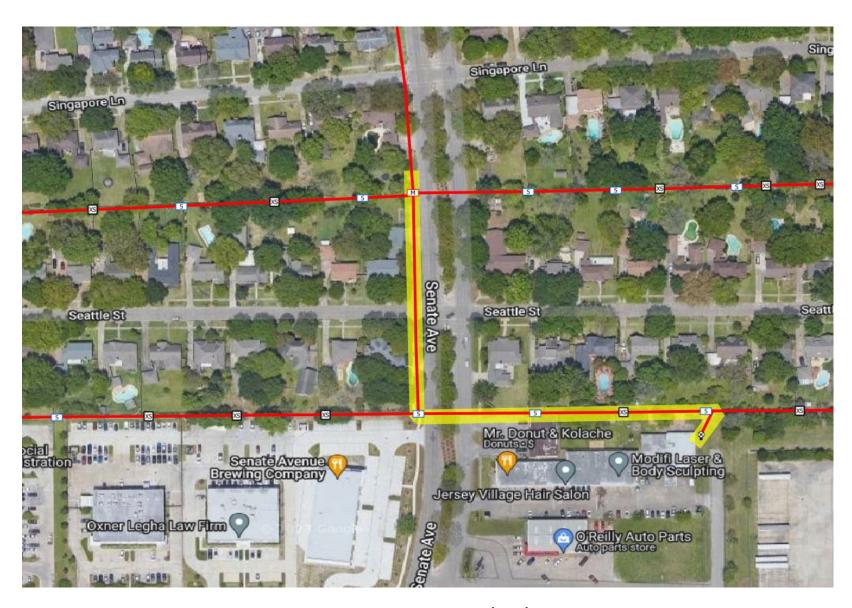

# **Underground Work**

- Conduit is already placed
- Crews will be placing handholes, flower-pots, and begin pulling fiber
- Rear Easements:
  - Philippine St
  - Colwyn Ln
  - Leeds Ln
  - Ashburton Dr
- Front Yard:
  - Ginger Ln
  - Philippine St
  - Argentina St



## **Underground Work**

- Most Conduit is already placed
- Crews will be placing handholes, flower-pots, and begin pulling fiber
- Rear Easements:
  - Koester St
- Tahoe Dr
- Rio Grande St
- Sierra Dr
- Achgill St
- Crawford St
- Smith St
- Carlsbad St
- Lewis St
- Capri Dr
- Hanley St
- Wall St

Kari Ct

Epernay Pl

- Kube Ct
- Senate Ave
- Kevindael Ct
- Elwood Dr
- Hawaii Ln
- Ginger Ln
- Honolulu St
- Yampa Ln
- Tenbury St




#### **Aerial Construction**

- This section should finish by 10/26
- Aerial Construction including tree trimming, setting anchors, and installing steel messenger cable continues
- As the steel messenger is placed, crews will begin placing fiber along the routes constructed over last few days
- Front Easement:
  - Senate Ave between Congo Ln & Jersey Dr
  - Lakeview Dr between
    Jersey Dr & Philippine St
- Rear Easement of:
  - Jersey Dr & Elwood Dr
  - Lakeview Dr & Zilonis Ct
  - Lakeview Dr & Leeds Ln



#### **Aerial Construction**

- Starting Early Next Week
- Aerial Construction including tree trimming, setting anchors, and installing steel messenger cable
- As the steel messenger is placed, crews will begin placing fiber along the routes constructed over last few days
- Rear Easement of:
  - Argentina St & Sam Houston Tollway

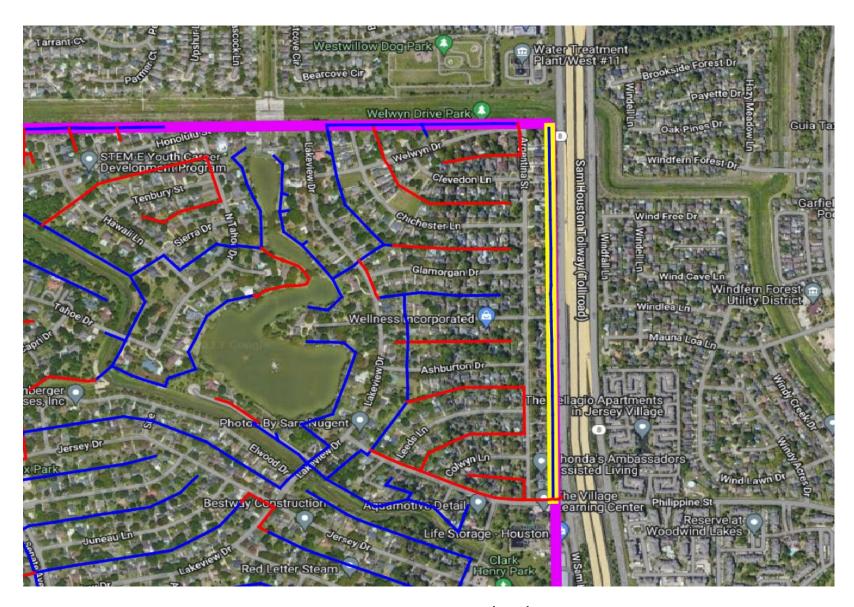

### **Cabinet Construction**

- Fiber Electronics Cabinet to be installed in ROW along Senate Ave Between Jersey Dr and Acapulco Dr
- Pouring Concrete Pad between
  10/23 10/28
- Excavating, trenching, placing handholes, placing duct, pulling fiber cables, installing electric service

