

ezee

F I B E R

***Jersey Village 3 Day Plan
11-29-2023***

Underground Work

- Boring, placing conduit, setting handholes, pulling fiber
- Rear Easements:
 - Both sides of DeLozier St
 - South side of Wall St
 - Rio Grande St



Underground Work

- Excavation is complete – Pulling Fiber and Splicing
- Rear Easements:
 - St Helier St & Cornwall St
 - St Helier & Jersey Dr
 - St. John Ct
 - Elwood Dr & Senate Ave
- Front Easement
 - Rio Grande St
 - Jersey Dr
 - Senate Ave




Underground Work

- Boring, placing conduit, setting handholes, pulling fiber
- Rear easement of Lakeview Dr & Acapulco Dr
- Rear Easement of Juneau Ln & Lakeview Dr
- Rear Easement of Lakeview Dr & Congo Ln




Underground Work

- Boring, placing conduit, setting handholes, pulling fiber
- Front easement of Australia St between Lakeview & Solomon
- Front easement of Solomon St between Australia and Shanghai
- Rear Easement of Congo Ln & Australia St
- Rear Easement of Shanghai St & Congo Ln

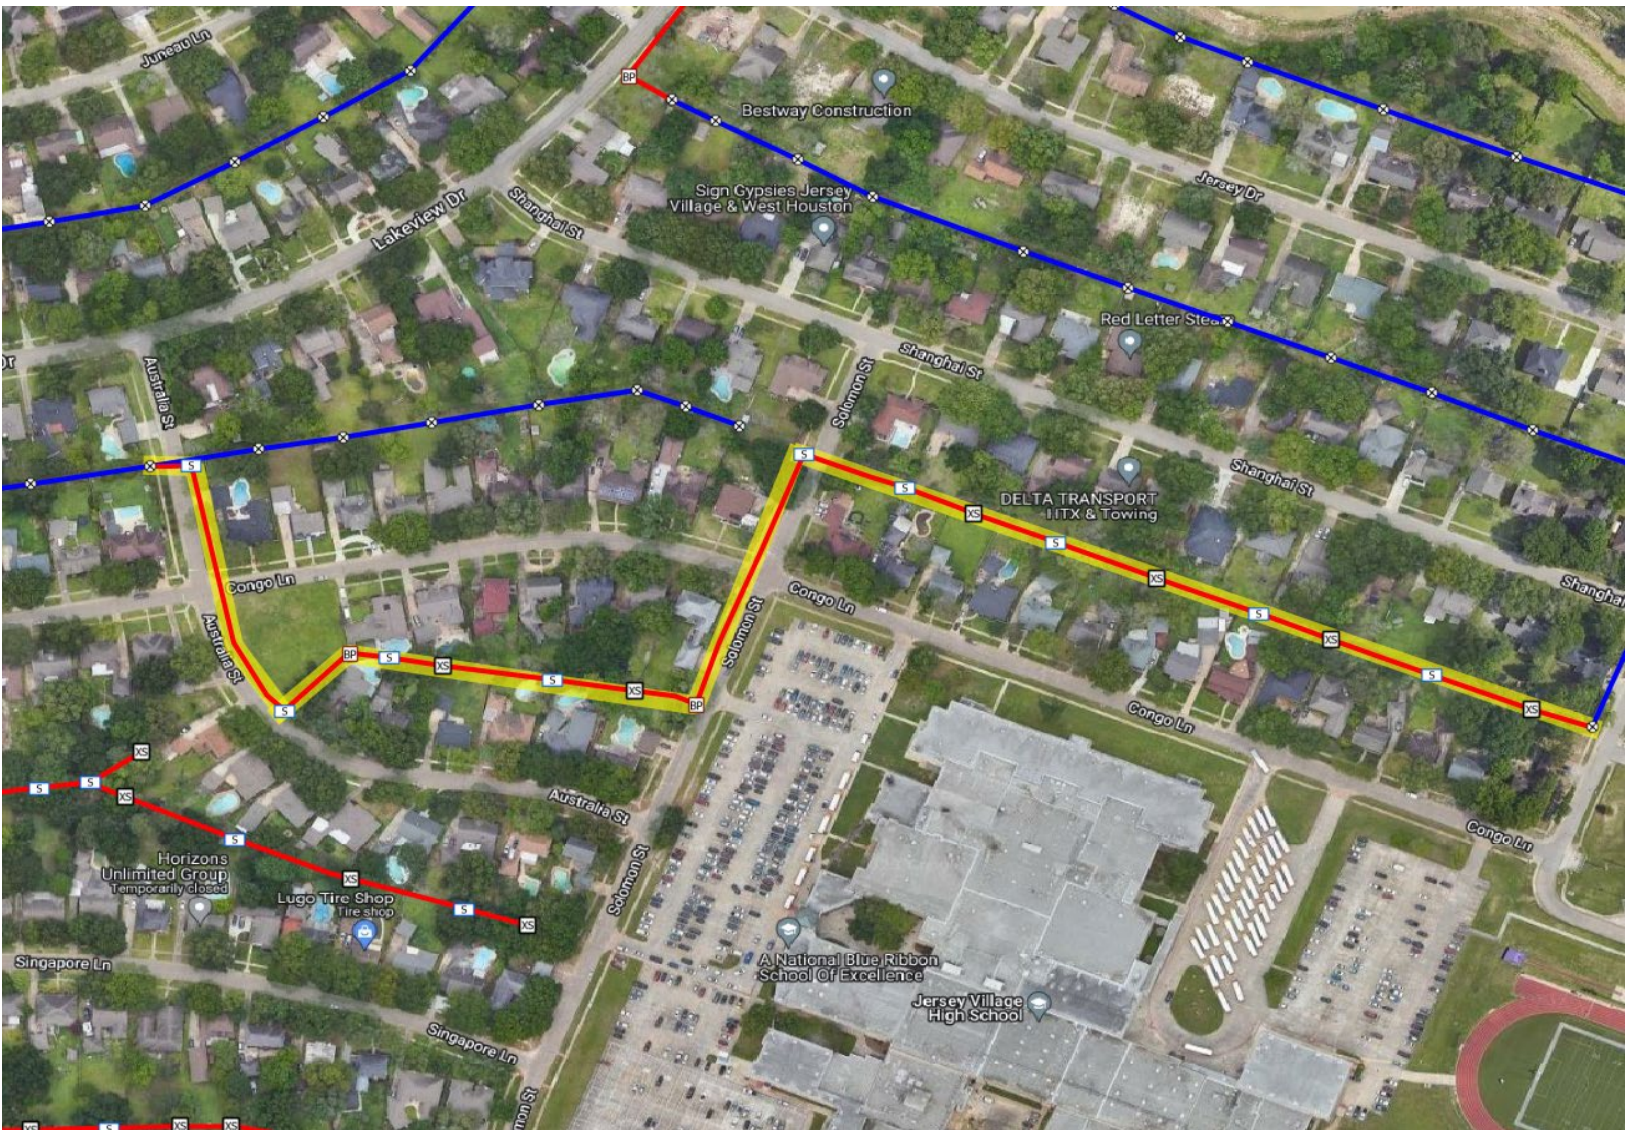


Aerial Construction

- Aerial Construction including tree trimming, setting anchors, and installing steel messenger cable
- Rear Easement of:
 - Hawaii Ln
 - Honolulu St
 - Sierra Dr
 - Tahoe Dr
 - Yampa Ln
- Front Easement
 - Hawaii Ln
 - Senate Ave
 - Tahoe Dr

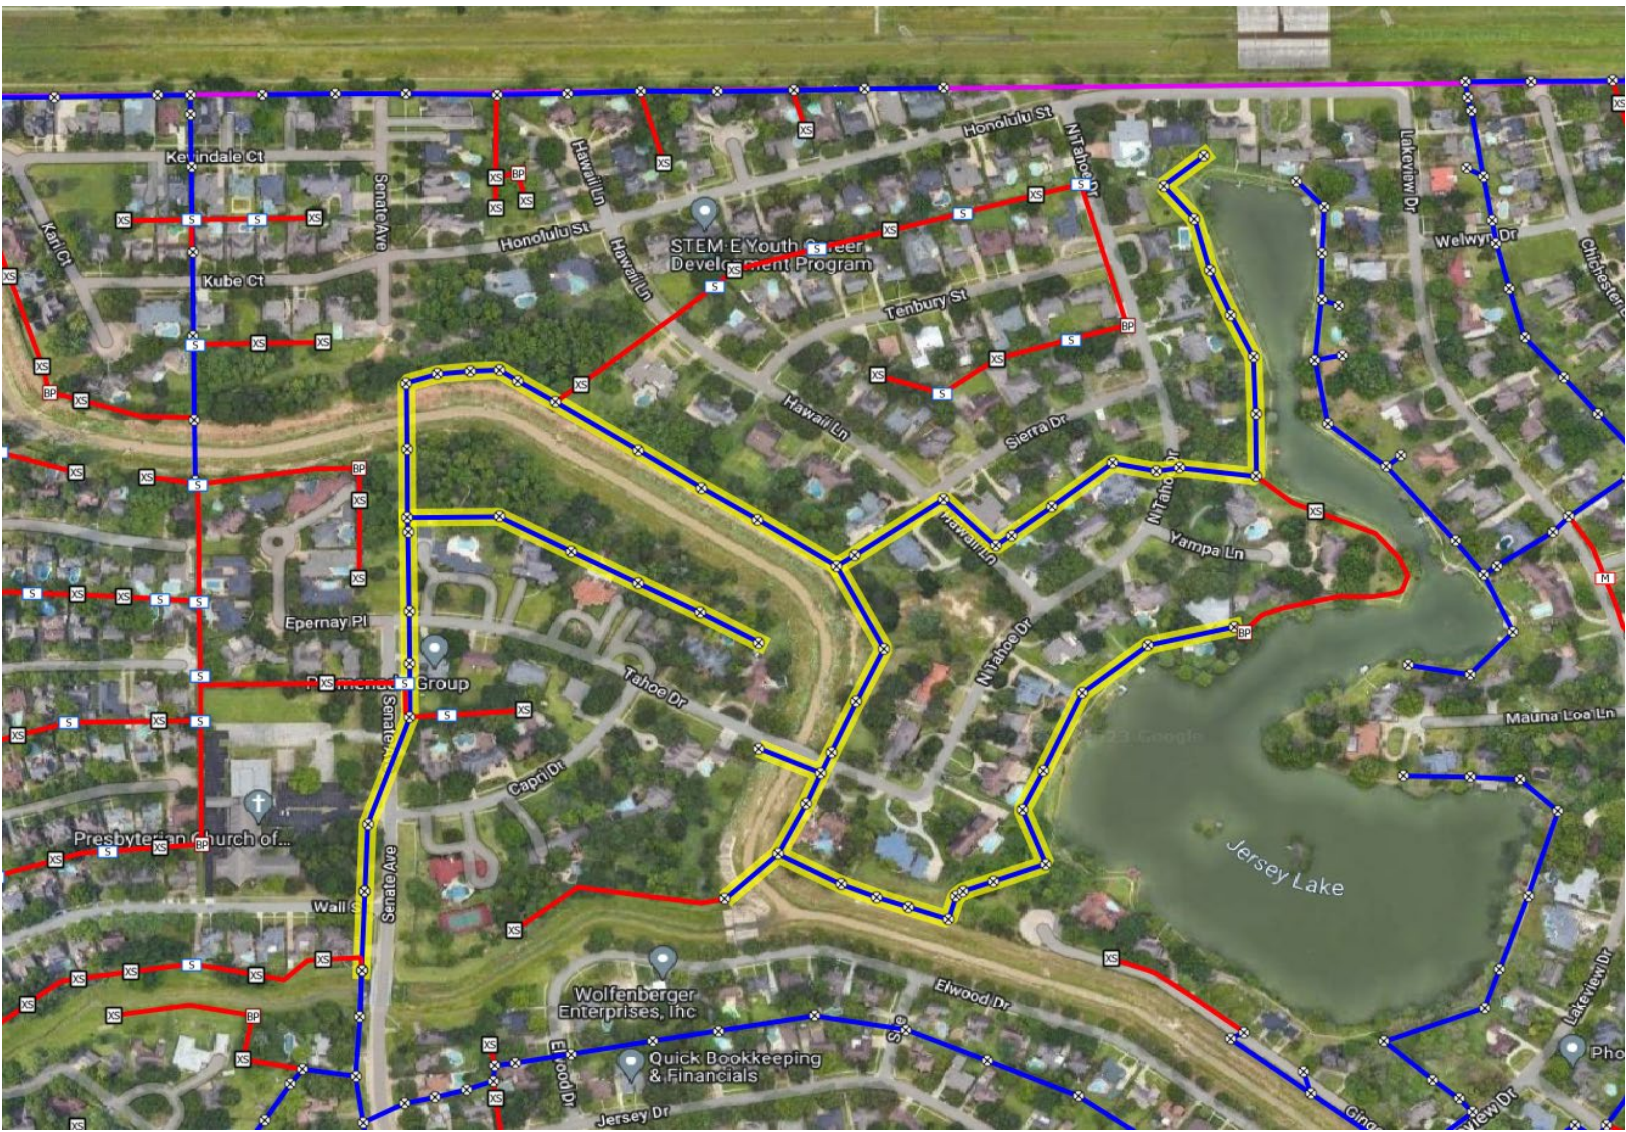

Aerial Construction

- Aerial Construction including tree trimming, setting anchors, and installing steel messenger cable continues
- As the steel messenger is placed, crews will begin placing fiber along the routes constructed over last few days
- Front Easement:
 - Senate Ave between Congo Ln & Jersey Dr
 - Lakeview Dr between Jersey Dr & Philippine St
- Rear Easement of:
 - Jersey Dr & Elwood Dr
 - Lakeview Dr & Zilonis Ct
 - Lakeview Dr & Leeds Ln

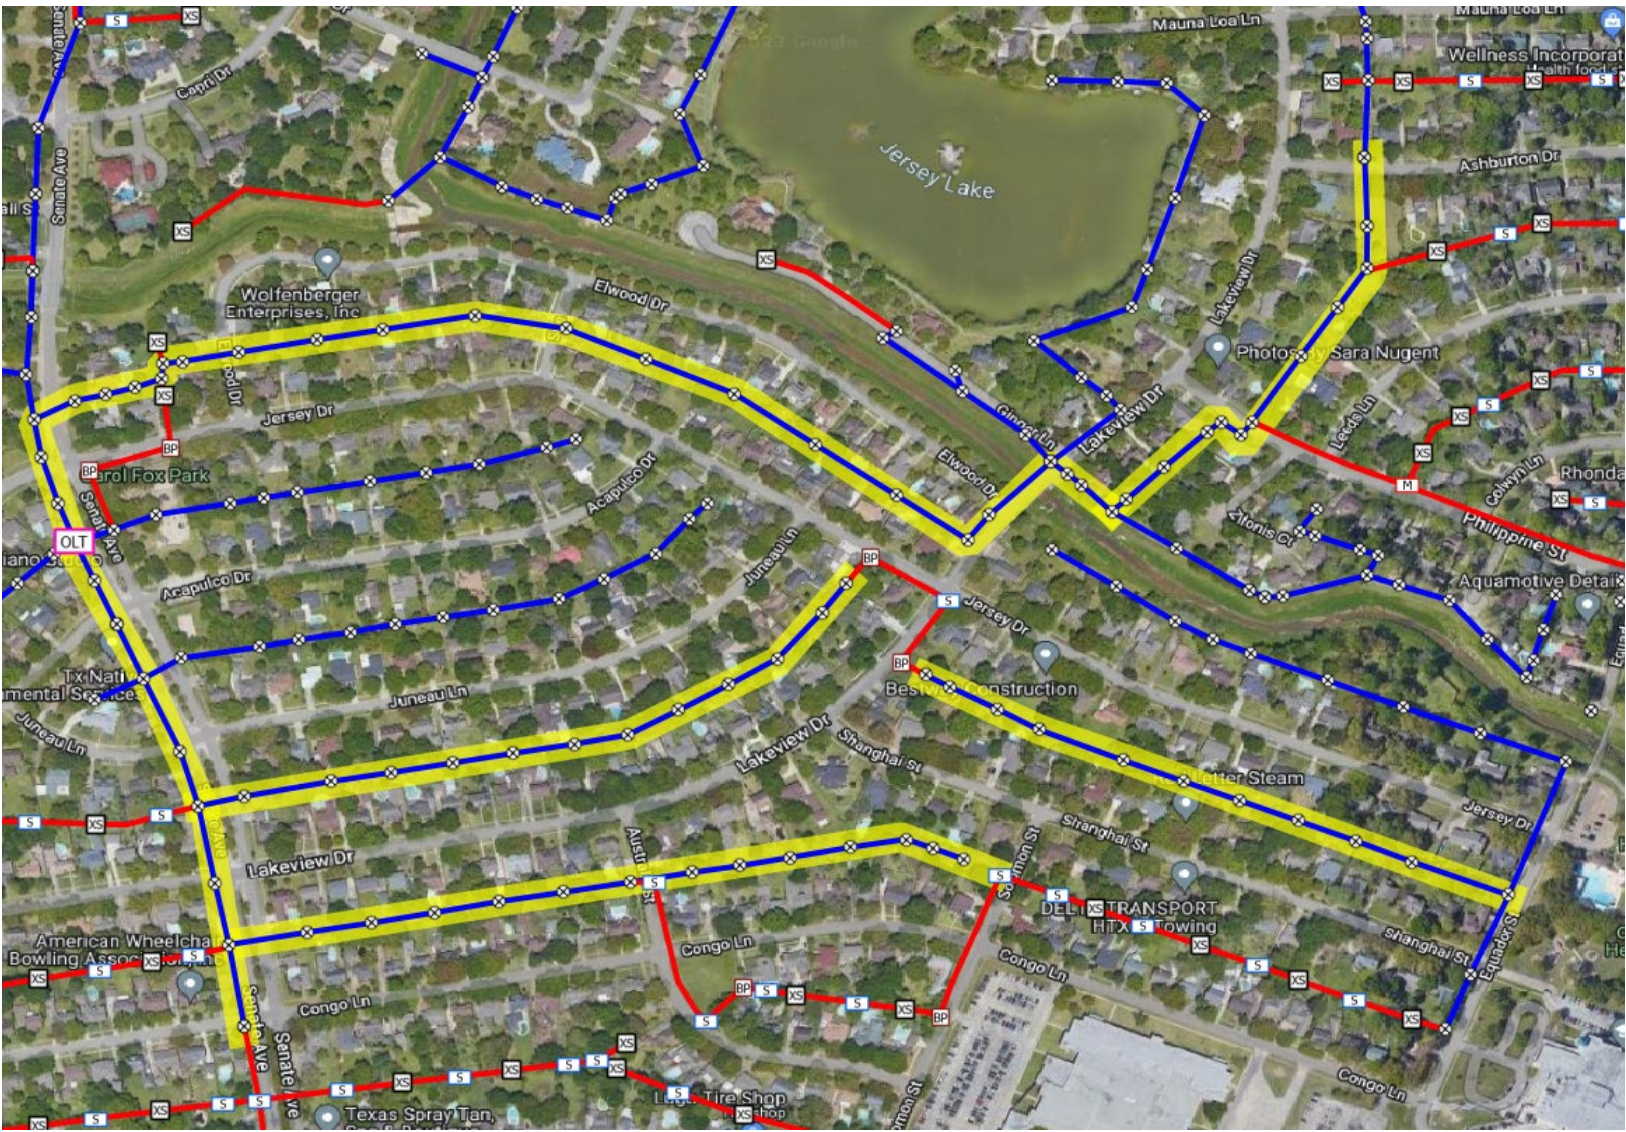

Aerial Construction

- Aerial Construction including tree trimming, setting anchors, and installing steel messenger cable
- Rear Easement of:
 - Argentina St & Sam Houston Tollway
 - Lakeview Dr
 - Zilonis Dr
 - Philippine St
 - Ecuador St
- Front Easement
 - Ginger Ln

