


Starting January 2nd/3rd of the New Year, we will be shifting traffic into Phase 2 Construction. Everyone that lives west of Carlsbad is strongly advised to use Carlsbad to get in or out to Senate Ave. This will allow each resident to get where they are going quicker as there will be construction traffic as well as residential traffic both ways east of Carlsbad. There will be flagged traffic during this time. Please be patient as we will do our best to keep traffic flowing throughout the project.

Starting January 3rd, a subcontractor will begin on constructing driveways west of Carlsbad starting with the driveways closest to Carlsbad and working towards the sound wall. 4 driveways will be removed at a time and will be prepared for concrete. The idea is to have 4 driveways removed and replaced in a span of 4-5 days. during construction of the driveways, the residents are welcome to park on the new pavement in front of their residence.

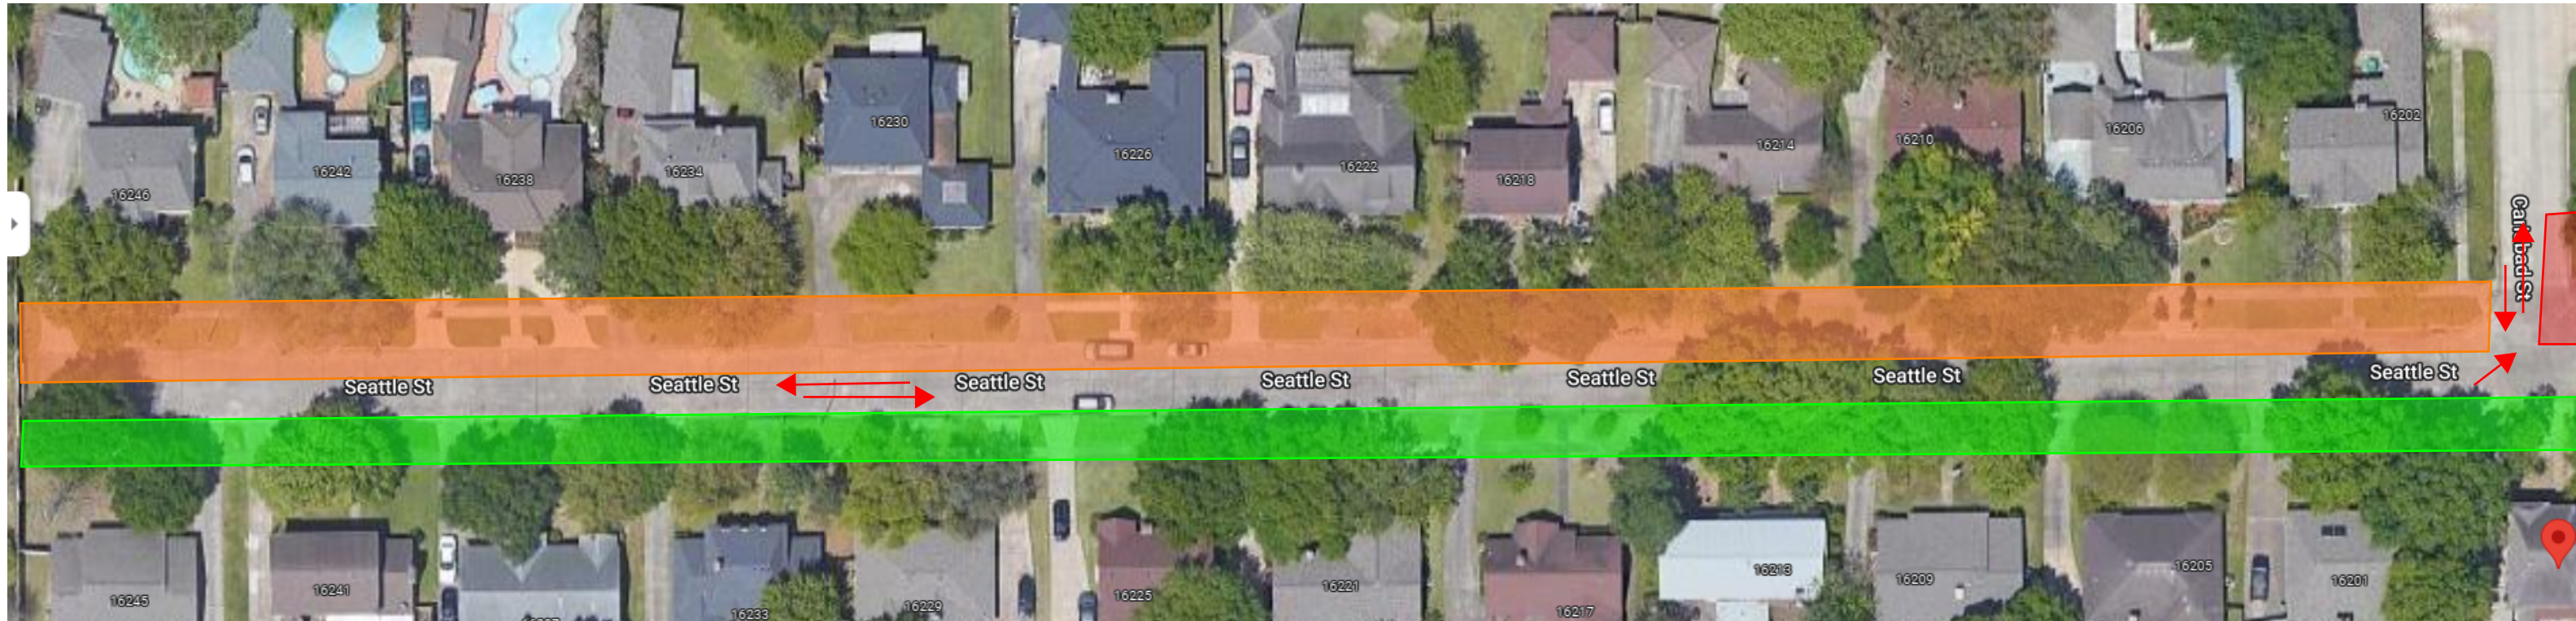

Starting the week of January 9th, the sanitary sewer subcontractor will begin on the sanitary heading west from Carlsbad to the sound wall. When the sanitary crew begins, we will be flagging traffic around their dirt piles on the street. The idea is to keep the driveway crew ahead of the sanitary crew on the north side of the street so when the sanitary crew catches up, the people across the road will already be back in their new driveway. Please be patient as this area will get congested with construction traffic.
