ID	Task Name	Duration	Start	Finish
1				
2	**Wall Street Subdivision - Jerse**	**355 days?**	**Mon 4/12/21**	**Sat 3/4/22**
3				
4	Mobilization	3 days	Mon 4/12/21	Wed 4/14/21
5	Traffic Control	2 days	Thu 3/18/21	Fri 3/19/21
6	Tree Protection	3 days	Sat 4/17/21	Sun 4/18/21
7	SWPPP	2 days	Mon 6/28/21	Tue 6/29/21
8				
9	**Wall Street**	**146 days?**	**Wed 4/21/21**	**Mon 9/13/21**
10	Remove Half of Existing	10 days	Wed 4/21/21	Fri 4/30/21
11	4' x 4' Junction Box - Sta	2 days	Sat 4/24/21	Sun 4/25/21
12	Tie into the existing 36" S	2 days	Mon 4/26/21	Tue 4/27/21
13	12' x 4' Junction Box - Sta	3 days	Wed 4/28/21	Fri 4/30/21
14	4' x 2' RCB	2 days	Sat 5/1/21	Mon 5/2/21
15	8' x 4' Junction Box - Sta	1 day	Tue 5/4/21	Tue 5/4/21
16	4' x 2' RCB	2 days	Wed 5/5/21	Thu 5/6/21
17	8' x 4' Junction Box	1 day	Fri 5/7/21	Fri 5/7/21
18	4' x 2' RCB	2 days	Sat 5/8/21	Sun 5/9/21
19	8' x 4' Junction Box	1 day	Mon 5/10/21	Mon 5/10/21
20	30" HDPE	2 days	Tue 5/11/21	Wed 5/12/21
21	Storm Manhole - Sta 30+	1 day	Thu 5/13/21	Thu 5/13/21
22	42" HDPE	2 days	Fri 5/14/21	Sat 5/15/21
23	Manhole - Sta 10+61	1 day?	Mon 5/16/21	Sun 5/16/21
24	42" HDPE	2 days	Mon 5/17/21	Tue 5/18/21
25	Manhole - Sta 10+55	1 day?	Wed 5/19/21	Wed 5/19/21
26	42" HDPE	3 days	Thu 5/20/21	Sat 5/22/21
27	Manhole - Sta 10+87	1 day?	Sun 5/23/21	Sun 5/23/21
28	42" HDPE	2 days	Mon 5/24/21	Tue 5/25/21
29	Manhole - Sta 13+55	1 day?	Wed 5/26/21	Wed 5/26/21
30	42" HDPE	2 days	Thu 5/27/21	Fri 5/28/21
31	Manhole - Sta 13+55	1 day	Sat 5/29/21	Sat 5/29/21
32	42" HDPE	2 days	Sun 5/30/21	Mon 5/31/21
33	Manhole - Sta 13+37	1 day?	Tue 6/1/21	Tue 6/1/21
34	42" HDPE	2 days	Wed 6/2/21	Fri 6/4/21
35	Manhole - Sta 11+93	1 day?	Sat 6/5/21	Sat 6/5/21
36	42" HDPE	3 days	Sun 6/6/21	Tue 6/8/21
37	Manhole - Sta 9+24	1 day?	Wed 6/9/21	Wed 6/9/21
38	42" HDPE	2 days	Thu 6/10/21	Fri 6/11/21
39	Manhole - Sta 8+52	1 day?	Sat 6/12/21	Sat 6/12/21
40	42" HDPE	3 days	Sun 6/13/21	Tue 6/15/21
41	Manhole - Sta 5+23	1 day?	Wed 6/16/21	Wed 6/16/21
42	42" HDPE	2 days	Thu 6/17/21	Fri 6/18/21
43	Manhole - Sta 3+18	1 day?	Sat 6/19/21	Sat 6/19/21
44	Tie into existing Storm Sy	2 days	Sun 6/20/21	Mon 6/21/21
45	42" HDPE	2 days	Tue 6/22/21	Wed 6/23/21
46	4' x 4' Junction Box	1 day?	Thu 6/24/21	Thu 6/24/21
47	42" HDPE	3 days	Fri 6/25/21	Sun 6/27/21
48	Manhole - Sta 0+57	1 day?	Mon 6/28/21	Mon 6/28/21
49	42" HDPE	2 days	Tue 6/29/21	Wed 6/30/21
50	Manhole - Sta 0+33	1 day?	Thu 7/1/21	Thu 7/1/21
51	42" HDPE	2 days	Fri 7/2/21	Sat 7/3/21
52	Manhole - Sta 2+55	1 day	Sun 7/4/21	Sun 7/4/21
53	42" HDPE	2 days	Mon 7/5/21	Tue 7/6/21
54	Manhole - Sta 1+73	1 day?	Wed 7/7/21	Wed 7/7/21
55	42" HDPE	4 days	Thu 7/8/21	Sun 7/11/21
56	Manhole - Sta 0+56	1 day?	Mon 7/12/21	Mon 7/12/21
57	42" HDPE	3 days	Tue 7/13/21	Thu 7/15/21
58	Manhole - Sta 0+55 North	2 days	Fri 7/16/21	Sat 7/17/21
59				
60	Liner Subgrade	1 day?	Fri 5/14/21	Fri 5/14/21
61	6" Concrete Pavement	20 days	Wed 5/19/21	Mon 6/7/21
62	Driveways & Sidewalks	20 days	Sat 5/29/21	Thu 6/17/21
63				
64	Remove North of Wall Str	5 days	Fri 6/18/21	Tue 6/22/21
65	Install Storm Leads and I	5 days	Wed 6/23/21	Sun 6/27/21
66	Liner Subgrade	10 days	Mon 6/28/21	Wed 7/7/21
67	6" Concrete Pavement	20 days	Sat 7/3/21	Thu 7/22/21
68	Driveways & Sidewalks	20 days	Tue 7/13/21	Wed 8/4/21
69	Sod & Clean Up	40 days	Thu 8/5/21	Mon 9/13/21
70				
71	**Crawford Street**	**115 days?**	**Sun 7/18/21**	**Tue 11/9/21**
72	4' x 2' RCB	2 days	Sun 7/18/21	Tue 7/20/21
73	8' x 4' Junction Box	1 day?	Wed 7/21/21	Wed 7/21/21
74	4' x 2' RCB	2 days	Thu 7/22/21	Fri 7/23/21
75	8' x 4' Junction Box	1 day?	Sat 7/24/21	Sat 7/24/21
76	30" HDPE	2 days	Sun 7/25/21	Mon 7/26/21
77	Manhole - Sta 8+00	1 day?	Tue 7/27/21	Tue 7/27/21
78	30" HDPE	2 days	Wed 7/28/21	Thu 7/29/21
79	Manhole - Sta 7+20	1 day?	Fri 7/30/21	Fri 7/30/21
80	30" HDPE	2 days	Sat 7/31/21	Sun 8/1/21
81	Manhole - Sta 7+08	1 day?	Mon 8/2/21	Mon 8/2/21
82	30" HDPE	2 days	Tue 8/3/21	Wed 8/4/21
83	Manhole - Sta 7+66	1 day?	Thu 8/5/21	Thu 8/5/21
84	30" HDPE	2 days	Fri 8/6/21	Sat 8/7/21
85	Manhole 6+28	1 day?	Sun 8/8/21	Sun 8/8/21
86	24" HDPE	5 days	Mon 8/9/21	Fri 8/13/21
87	Storm Manhole - Sta 5+	2 days	Sat 8/14/21	Sun 8/15/21
88	24" HDPE	5 days	Mon 8/16/21	Fri 8/20/21
89	Storm Manhole - Sta 3+	2 days	Sat 8/21/21	Sun 8/22/21
90	24" HDPE	5 days	Mon 8/23/21	Fri 8/27/21
91	Storm Manhole - Sta 1+	2 days	Sat 8/28/21	Sun 8/29/21
92				
93	Liner Subgrade	5 days	Thu 8/5/21	Mon 8/9/21
94	6" Concrete Pavement	30 days	Tue 8/10/21	Wed 9/8/21
95	Driveways & Sidewalks	30 days	Fri 8/20/21	Sat 9/18/21
96				
97	Remove North of Wall Str	5 days	Sun 9/19/21	Thu 9/23/21
98	Install Storm Leads and I	2 days	Fri 9/24/21	Sat 9/25/21
99	Liner Subgrade	5 days	Sun 9/26/21	Thu 9/30/21
100	6" Concrete Pavement	30 days	Fri 10/1/21	Sat 10/30/21
101	Driveways & Sidewalks	30 days	Mon 10/11/21	Tue 11/9/21
102				
103	**Carlstad Street**	**169 days**	**Tue 8/11/21**	**Tue 12/28/21**
104	4' x 2' RCB	5 days	Tue 8/11/21	Sat 8/15/21
105	8' x 4' Junction Box - Sta	1 day	Sun 8/16/21	Sun 8/16/21
106	6" Concrete Paving with	40 days	Sun 8/16/21	Tue 9/28/21
107	42" HDPE	3 days	Mon 8/30/21	Wed 9/1/21
108	4' x 4' Junction Box - Sta	1 day	Thu 9/2/21	Thu 9/2/21
109	42" HDPE	4 days	Fri 9/3/21	Mon 9/6/21
110	Storm Manhole - Sta 9+0	1 day	Tue 9/7/21	Tue 9/7/21
111	42" HDPE	4 days	Wed 9/8/21	Sat 9/11/21
112	Storm Manhole - Sta 8+	1 day	Sun 9/12/21	Sun 9/12/21
113	Storm Manhole - Sta 12+	1 day	Mon 9/13/21	Mon 9/13/21
114				
115	Liner Subgrade	10 days	Tue 9/14/21	Thu 9/23/21
116	6" Concrete Pavement	20 days	Sun 9/19/21	Wed 10/13/21
117	Driveways & Sidewalks	20 days	Wed 9/29/21	Sat 10/23/21
118	Sod & Clean Up	3 days	Sun 10/24/21	Tue 10/26/21
119				
120	**Tallow Street**	**36 days?**	**Tue 9/14/21**	**Tue 10/19/21**
121	30" Storm Sewer	2 days	Tue 9/14/21	Wed 9/15/21
122	Storm Manhole - Sta 13+	1 day?	Thu 9/16/21	Thu 9/16/21
123	30" HDPE	2 days	Fri 9/17/21	Sat 9/18/21
124	Storm Manhole - Sta 12+	1 day?	Sun 9/19/21	Sun 9/19/21
125	30" HDPE	2 days	Mon 9/20/21	Tue 9/21/21
126	Storm Manhole - Sta 9+2	1 day?	Wed 9/22/21	Wed 9/22/21
127				
128	Liner Subgrade	2 days	Thu 9/23/21	Fri 9/24/21
129	6" Concrete Pavement	5 days	Sat 9/25/21	Wed 9/29/21
130	Driveways & Sidewalks	5 days	Thu 9/30/21	Mon 10/4/21
131				
132	Remove North of Wall Str	2 days	Tue 10/5/21	Wed 10/6/21
133	Install Storm Leads and I	1 day?	Thu 10/7/21	Thu 10/7/21
134	Liner Subgrade	2 days	Fri 10/8/21	Sat 10/9/21
135	6" Concrete Pavement	5 days	Sun 10/10/21	Thu 10/14/21
136	Driveways & Sidewalks	5 days	Fri 10/15/21	Tue 10/19/21
137				
138				
139	**Capri Drive**	**87 days?**	**Sun 7/18/21**	**Wed 9/22/21**
140	30" HDPE	2 days	Sun 7/18/21	Mon 7/19/21
141	Storm Manhole - Sta 10+	1 day?	Tue 7/20/21	Tue 7/20/21
142	30" HDPE	2 days	Wed 7/21/21	Thu 7/22/21
143	Storm Manhole - Sta 9+0	1 day?	Fri 7/23/21	Fri 7/23/21
144	30" HDPE	2 days	Sat 7/24/21	Sun 7/25/21
145	Storm Manhole - Sta 8+0	1 day?	Mon 7/26/21	Mon 7/26/21
146	30" HDPE	2 days	Tue 7/27/21	Wed 7/28/21
147	Storm Manhole - Sta 7+0	1 day?	Thu 7/29/21	Thu 7/29/21
148	30" HDPE	2 days	Fri 7/30/21	Sat 7/31/21
149	Storm Manhole - Sta 6+0	1 day?	Sun 8/1/21	Sun 8/1/21
150	30" HDPE	2 days	Mon 8/2/21	Tue 8/3/21
151	Storm Manhole - Sta 5+0	1 day?	Wed 8/4/21	Wed 8/4/21
152	30" HDPE - Sta 3+65	2 days	Thu 8/5/21	Fri 8/6/21
153	Storm Manhole - Sta 3+1	1 day?	Sat 8/7/21	Sat 8/7/21
154	30" HDPE	2 days	Sun 8/8/21	Mon 8/9/21
155	Storm Manhole - Sta 1+1	1 day?	Tue 8/10/21	Tue 8/10/21
156	30" HDPE	2 days	Wed 8/11/21	Thu 8/12/21
157	Storm Manhole - Sta 1+1	1 day?	Fri 8/13/21	Fri 8/13/21
158	30" HDPE	2 days	Sat 8/14/21	Sun 8/15/21
159	Storm Manhole - Sta 1+1	1 day?	Mon 8/16/21	Mon 8/16/21
160				
161	Liner Subgrade	5 days	Tue 8/17/21	Sat 8/21/21
162	6" Concrete Pavement	10 days	Thu 8/19/21	Sat 8/28/21
163	Driveways & Sidewalks	8 days	Tue 8/24/21	Tue 8/31/21
164				
165	Remove North of Wall Str	2 days	Wed 9/1/21	Thu 9/2/21
166	Install Storm Leads and I	2 days	Fri 9/3/21	Sat 9/4/21
167	Liner Subgrade	5 days	Sun 9/5/21	Thu 9/9/21
168	6" Concrete Pavement	10 days	Tue 9/7/21	Thu 9/16/21
169	Driveways & Sidewalks	8 days	Sun 9/12/21	Sun 9/19/21
170	Sod & Clean Up	3 days	Mon 9/20/21	Wed 9/22/21
171				
172	**Pump Station**	**247 days**	**Tue 6/1/21**	**Wed 2/23/22**
173	Excavation	7 days	Tue 6/1/21	Mon 6/7/21
174	Form and Setup for the P	60 days	Tue 6/8/21	Fri 8/6/21
175	Dual Basin	60 days	Mon 6/7/21	Thu 8/5/21
176	Install Pumps	7 days	Mon 12/20/21	Sun 12/26/21
177	Install Generator	10 days	Mon 12/27/21	Wed 1/5/22
178	Electrical Services	20 days	Thu 1/6/22	Sun 1/23/22
179	Fence and Gate	3 days	Mon 1/31/22	Wed 2/2/22
180				
181	Restoration & Demobilization	3 days	Thu 2/3/22	Sat 2/5/22

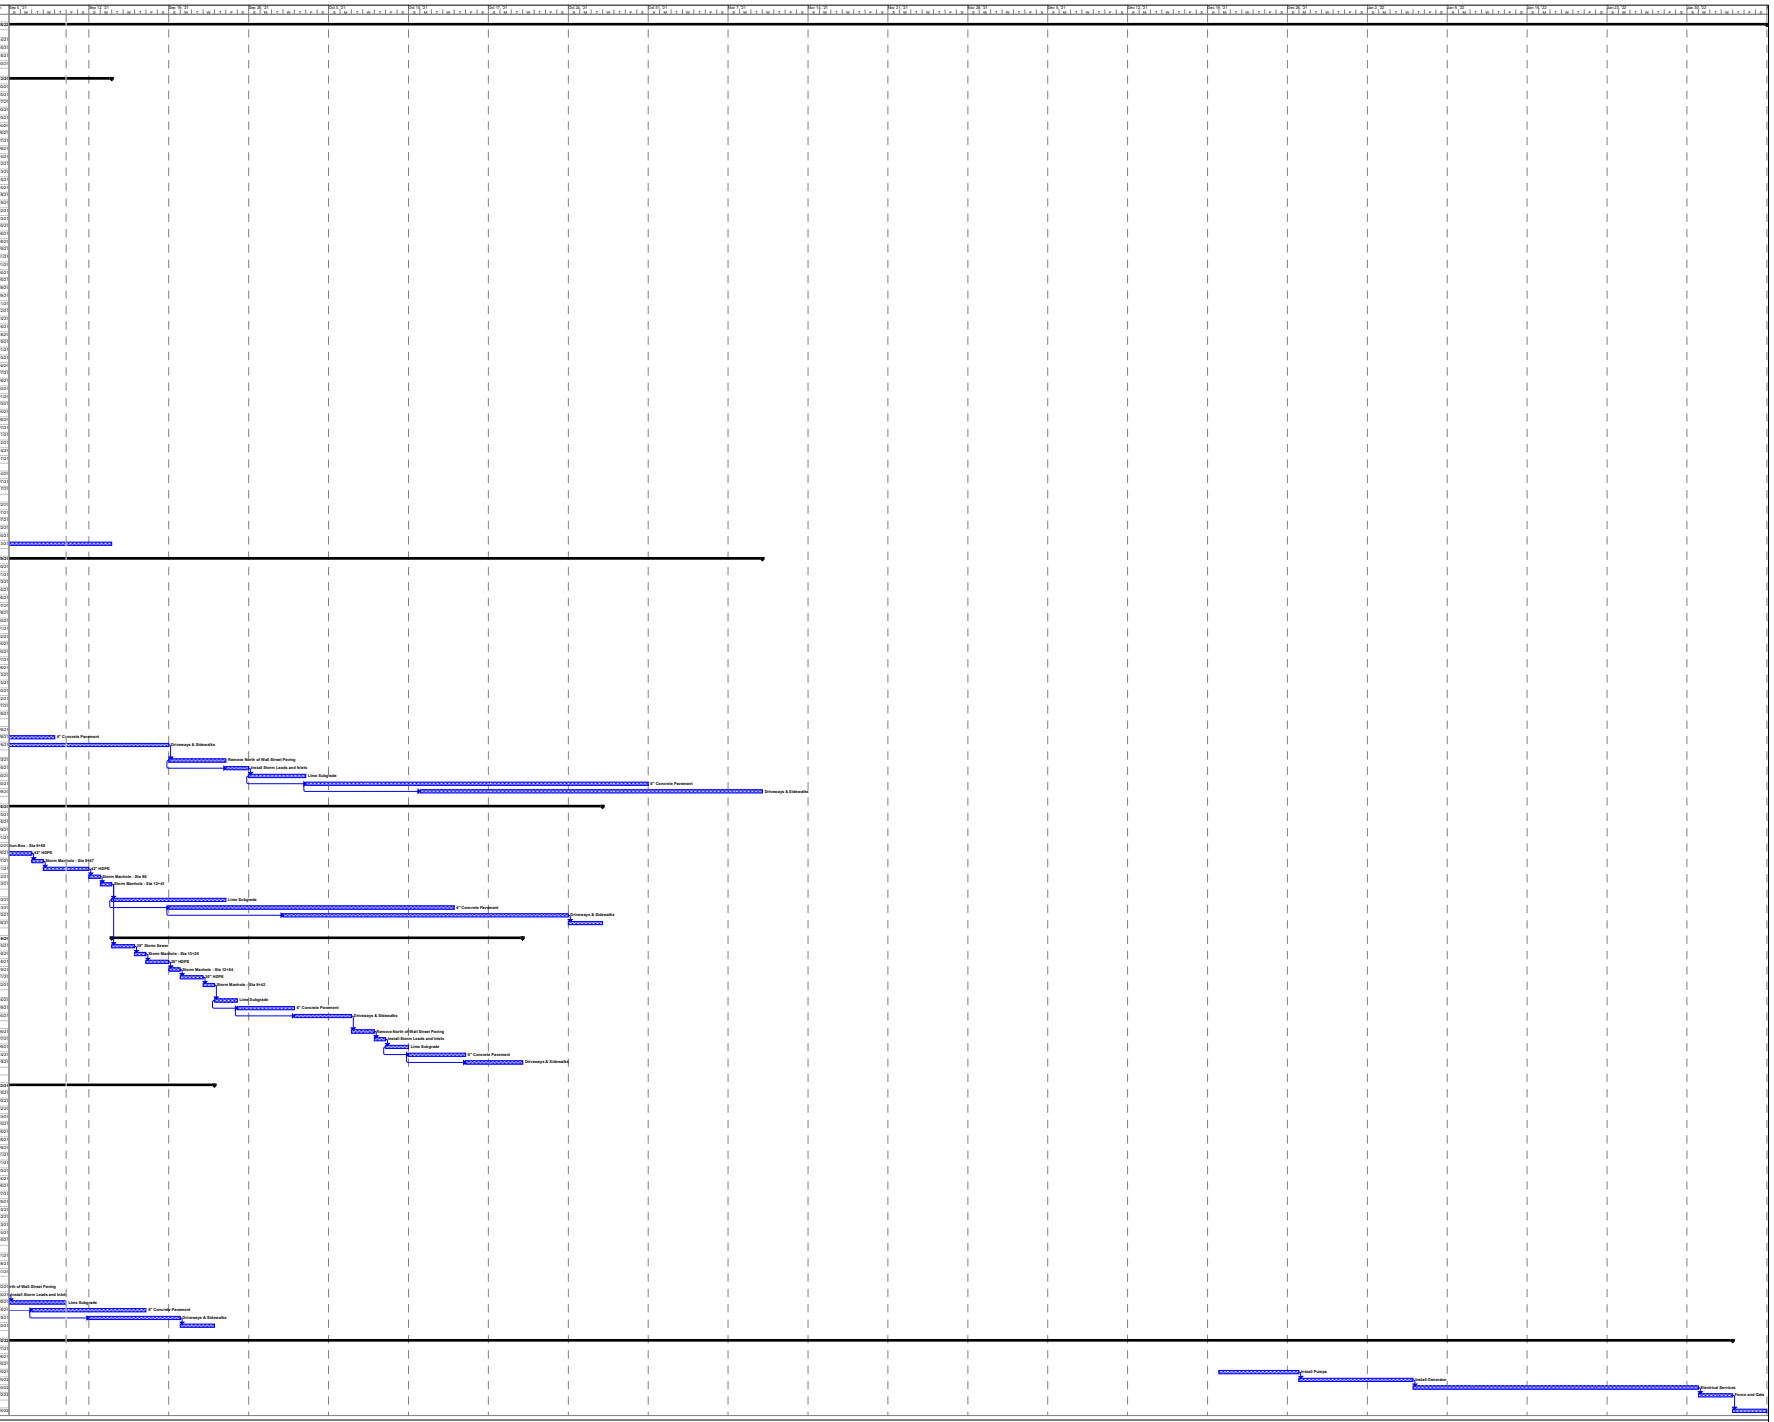

Project: Wall Street - Jersey Village Sy
Date: Fri 6/18/21

Task | Split | Milestone | Summary | Project Summary | External Tasks | External Milestone | Inactive Task | Inactive Milestone | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Progress | Deadline
